

Facilities & Construction Report

PROJECT STATUS 1/22/2018

- **New Construction**
 - Laughlin Elementary STEM Magnet School
 - Stadium Bleacher Project
 - Early College High School Asphalt
- **Technology**
 - Service Desk - Monthly Report
- **Maintenance**
 - Service Desk - Monthly Report
 - Sustainability Plan
 - Campus Painting Project
 - Campus Repairs
 - High School Library
 - Campus Upgrades
 - Playground Installations

New Construction

Laughlin Elementary STEM Magnet School



- ✦ **Ground Breaking – 12/12/2017**
- ✦ **Electrical Service “On Order” – 1/7/2018**
- ✦ **Building Pads – Completed – 1/11/2018**
- **Walkways, Ramps, & Utilities – 1/22/2018**
- **Modular Building Delivery - Scheduled – 2/12/2018 – 2/22/2018**

New Construction

Walter Levermann Ram Stadium – Guest Bleachers



- ❑ Pending Approval of Bid – 1/22/2018
- ❑ Demolition of Legacy Bleachers – T.B.D.
- ❑ Installation of New Bleachers – T.B.D.
- ❑ Schematic Drawings of Storage, Restrooms, and Concession Stand – March 2018

New Construction


Early College High School Asphalt Project



Parking Lot will Reopen 1/23/2018

Technology

Support Tickets 12-1-2017 thru 1-1-2018

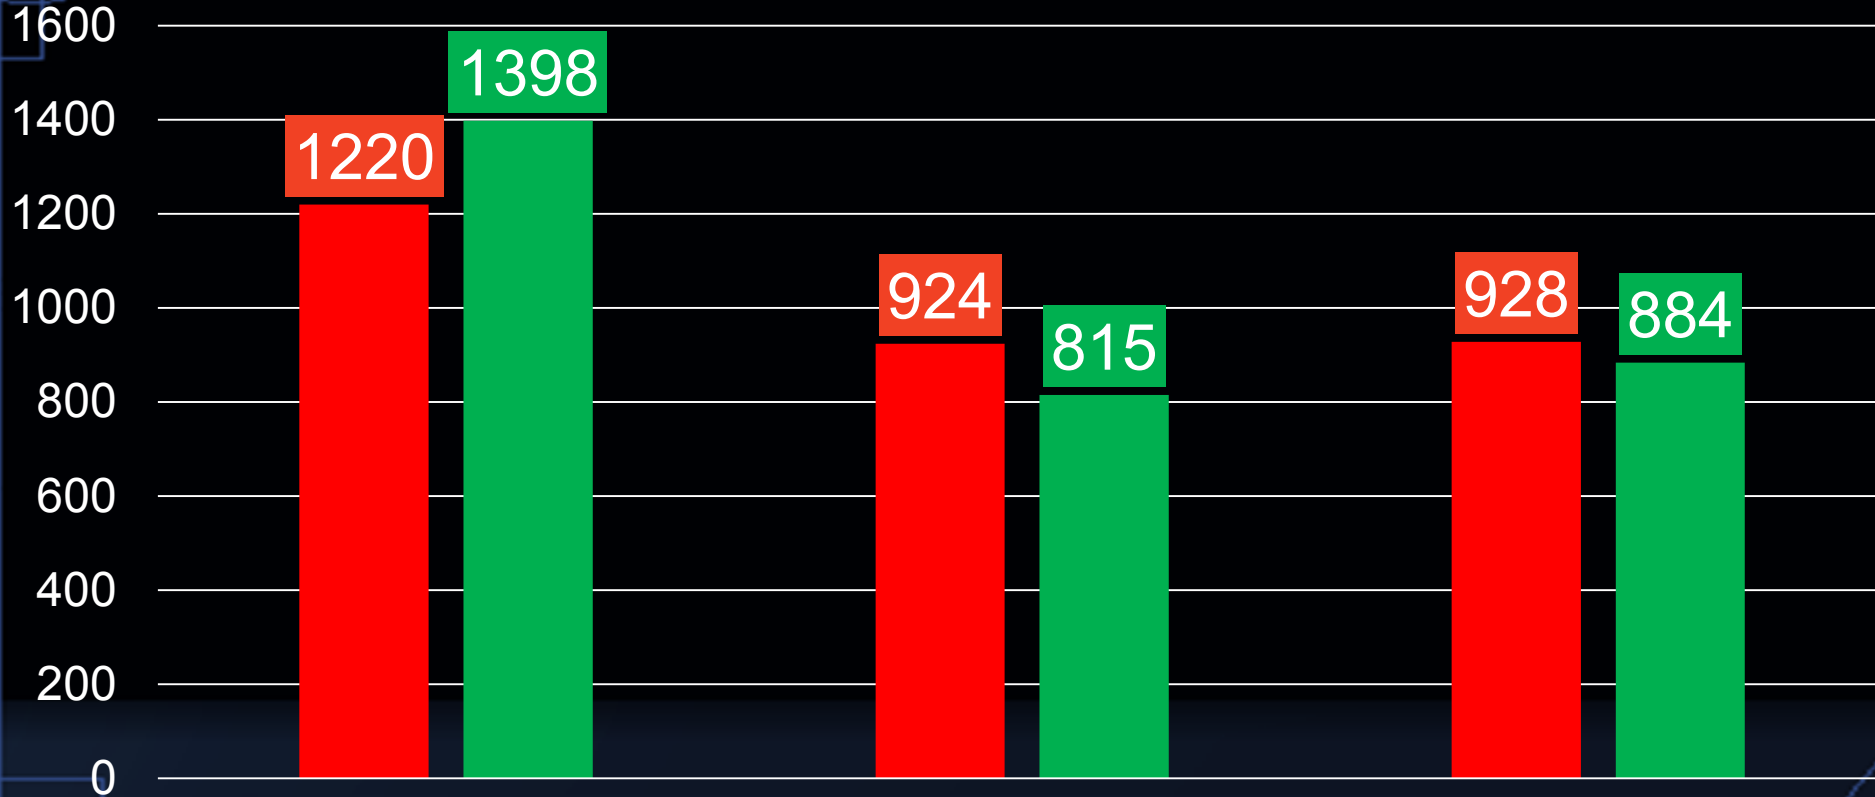

Created Tickets = 928
Projects = 25
In Progress = 19
Completed = 884


30 Days = 44
60 Days = 109
90 Days = 6

October November December

■ Tickets Created ■ Tickets Completed

Maintenance

Support Tickets 12-1-2017 thru 1-1-2018



Created Tickets = 375
Completed = 317

30 Days = 58
60 Days = 74

October November December

■ Tickets Created ■ Tickets Completed

Maintenance – Sustainability Plan

Painting Project Status

Ruben Chavira



North Heights Elementary



- Garfield “Exterior” – Completed
- Ruben Chavira “Exterior” – Completed
- Ruben Chavira “Interior” – June 11th 2018
- North Heights “Interior” – July 16th 2018 - Tentative

Maintenance – Campus Repairs


Del Rio High School

- Library Plumbing Issues



Maintenance – Campus Upgrades

Playground Installations

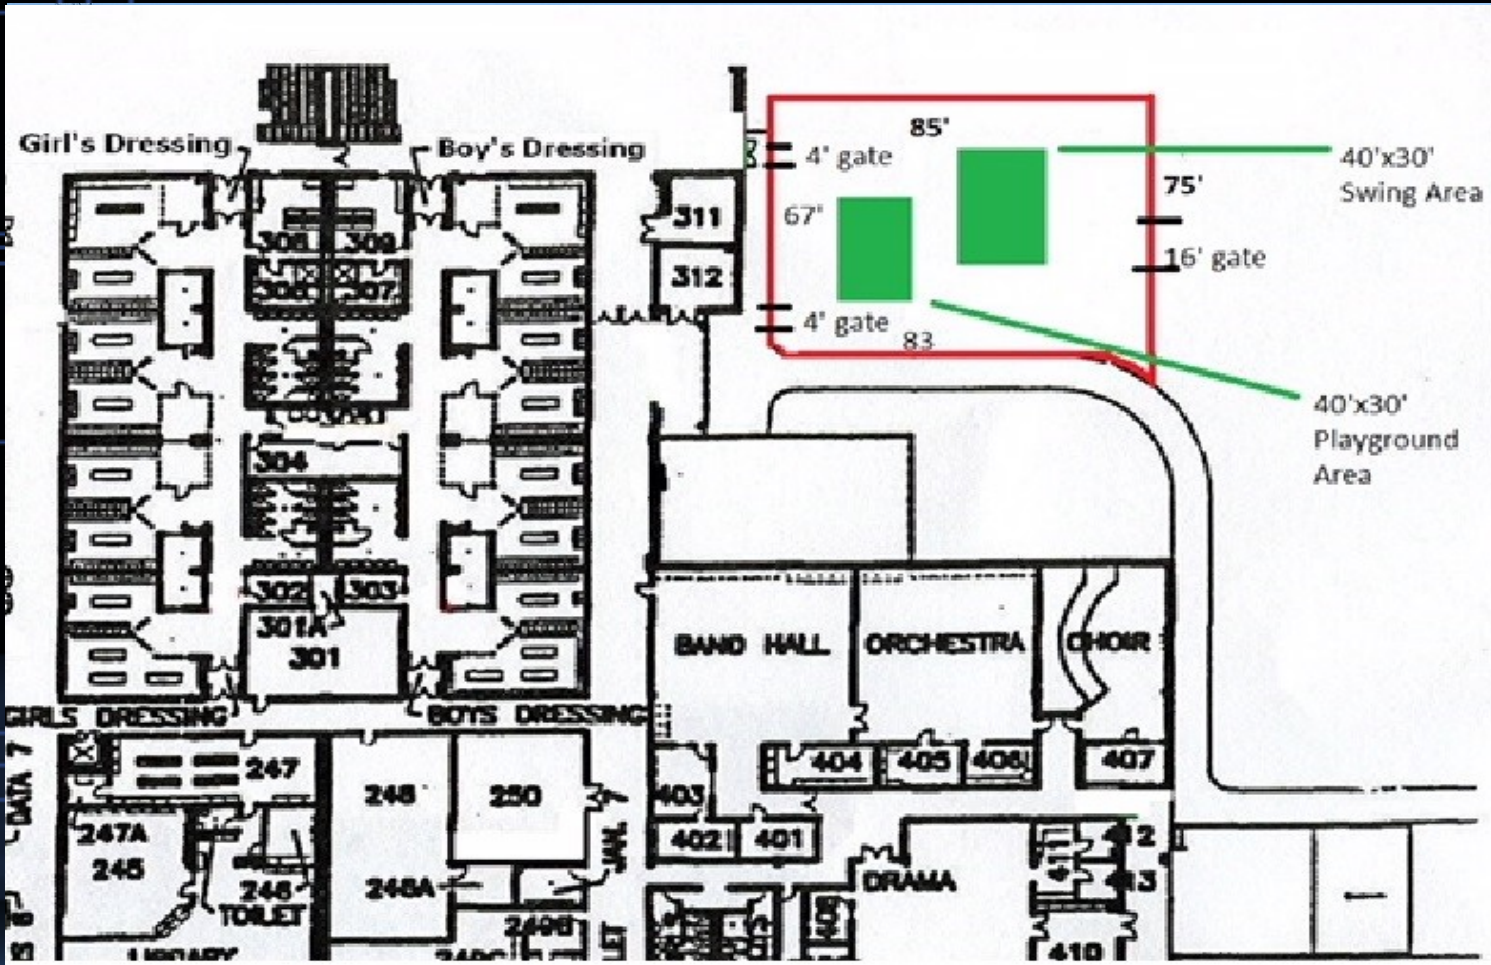

- Deployment Status
 - ▣ Cardwell - Completed
 - ▣ Chavira - Completed
 - ▣ Calderon – Completed
 - ▣ Del Rio Middle School – Design
 - ▣ North Heights – Design Phase

The background is a dark blue gradient with white geometric lines and shapes. On the left, there is a vertical line with a circle at the top. On the right, there are several overlapping rectangular and circular shapes. The overall style is modern and technical.

Questions?
