

# Facilities & Construction Report

**PROJECT STATUS 3/19/2018**

# Operations @ A Glance

- New Construction
  - Laughlin Elementary STEM Magnet School
  - Stadium Bleacher Project
  - Portable Buildings
- Technology Department
  - Monthly Service Requests
- Maintenance Department
  - Austin Campus Renovation
  - Campus Improvements - DRMS
  - Monthly Service Requests

# New Construction

## Laughlin Elementary STEM Magnet School

- ✓ Arrival of first modular - 2-16-18
- ✓ Set crew arrives to join buildings - 2-23-18
- ✓ Set crew finishes - 3-15-18
- Technology Cable Installation – In Progress
- Walkways and parking lot finish - 4-1-18
- Interior work, data intercom - 5-1-18
- Security finished - 5-1-18
- Complete all work - 5-15-18



# New Construction

## Walter Levermann Ram Stadium – Bleachers




- ✓ Board Approved – 1/22/2018
- ✓ Demo of Bleachers - Scheduled – 2/12/2018 – Delayed (Rescheduled to 2/19/2018)
- Schematic Drawings of Storage, Restrooms, and Concession Stand – March 2018
- Cement Footings being installed – April 2018
- Installation of New Bleachers – 5/1/2018



# New Construction


## Surplus Portable Buildings

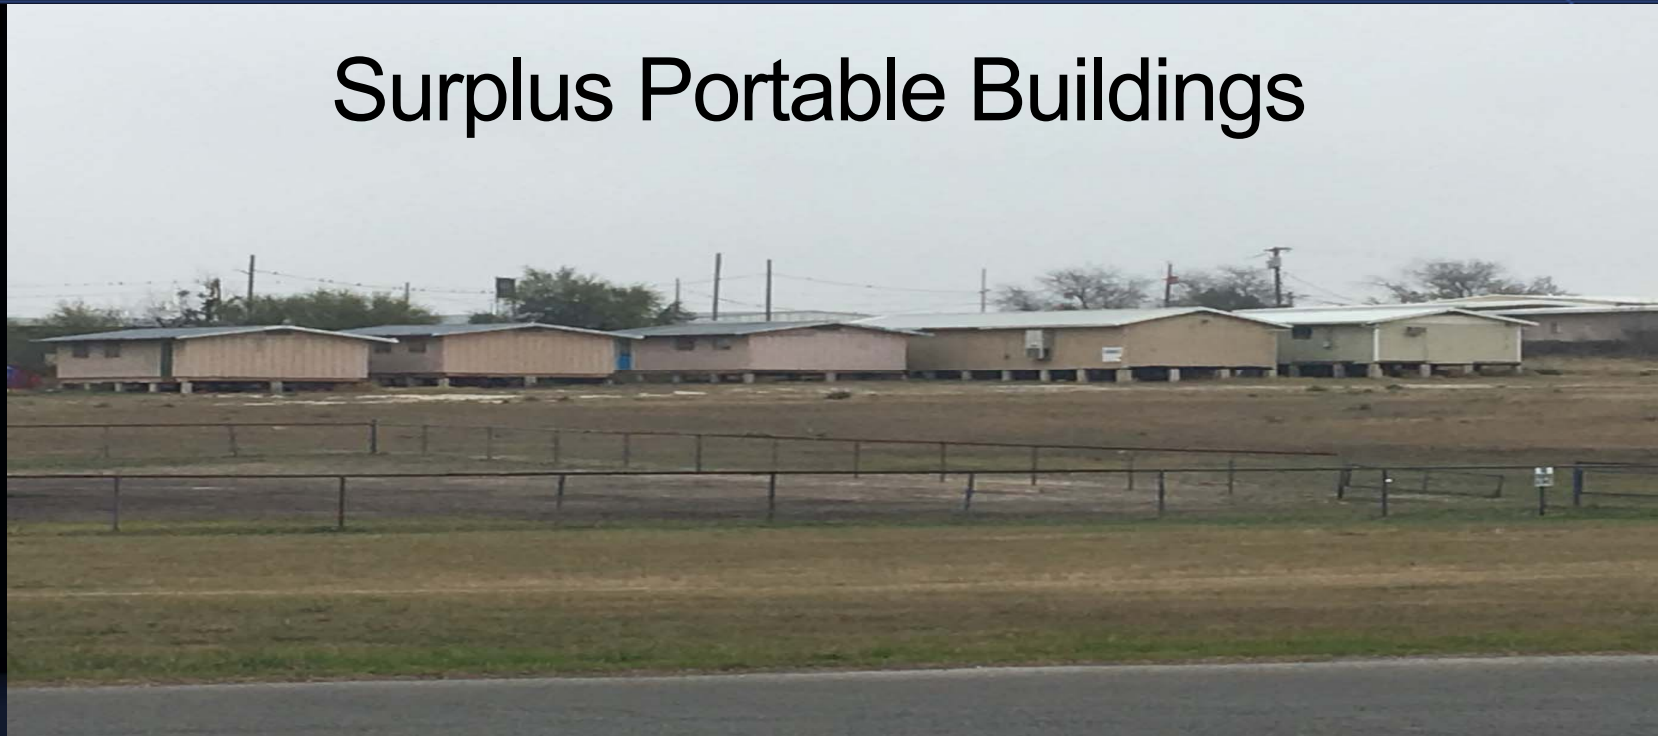

- 2/1/2018 – 4/1/2018 Portable Clean Up
- ✓ 3/9/2018 – Establish Moving Options
- 3/25/2018 – Publish Portables – News Herald
- 5/1/2018 – Proceed with Removal or Abatement

# Technology Department – Monthly Service Requests

Support Tickets 2-1-2018 thru 3-1-2018

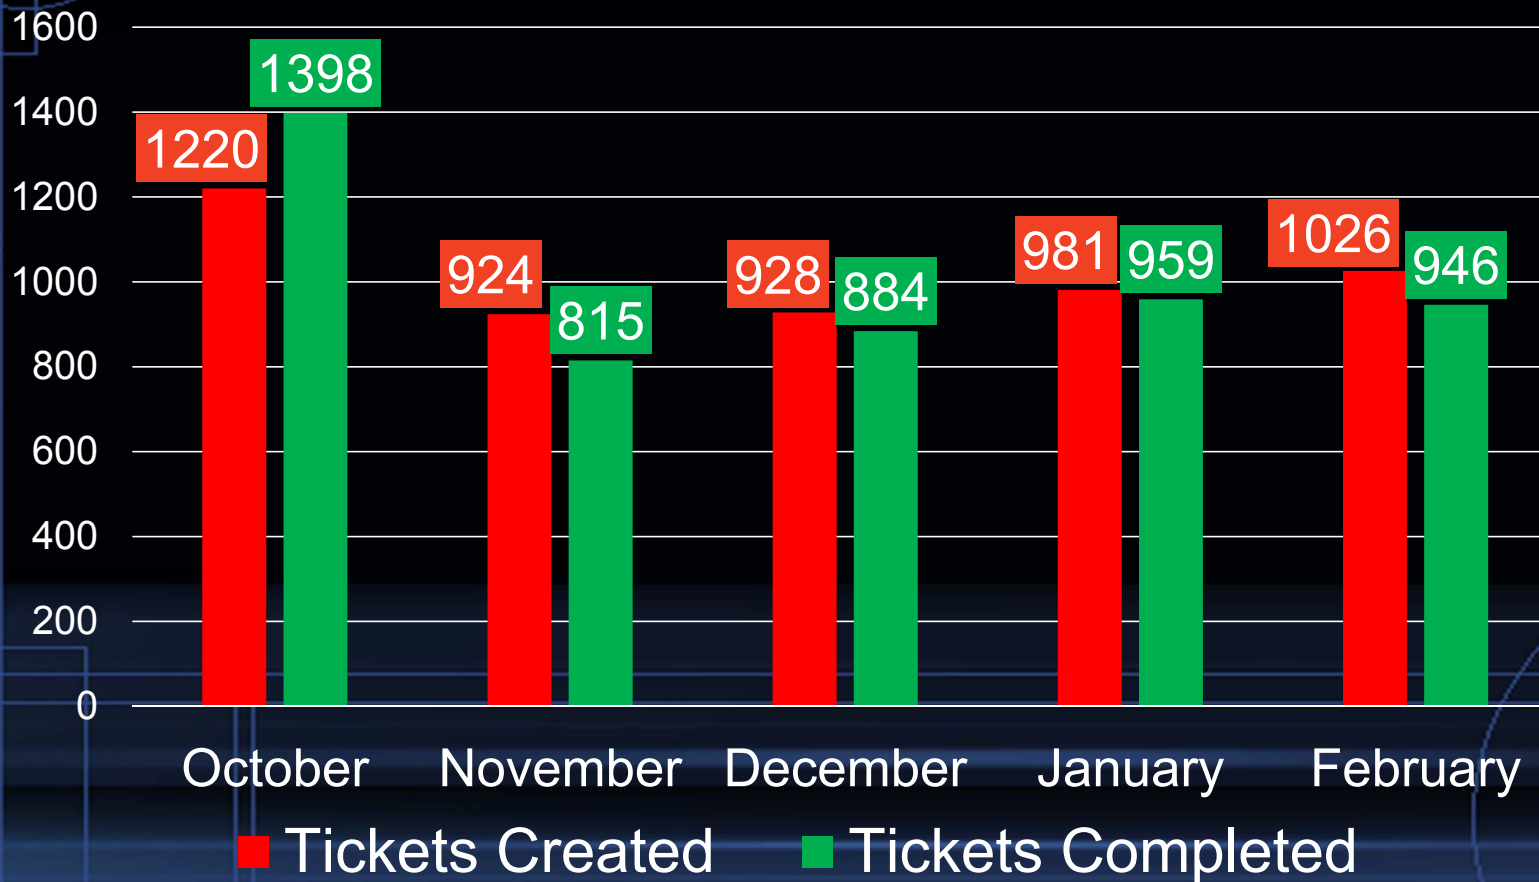

Within 30 Days = 80  
60 Days = 0  
90 + Days = 0

# Maintenance Department

## Austin Campus – Renovations



- Maintenance Office (Awaiting Furniture)
- Trade Moves
  - Electricians – 80% Completed
  - Painters – 90% Completed
  - HVAC – 70% Completed
  - Plumbing – Pending
  - Carpentry - Pending
- Technology Office (Scheduled June 1<sup>st</sup>)
  - Call Center
  - Computer Technicians
  - Cable Team
  - Network Specialist / Admins



# Maintenance Department

## Campus Improvements – Del Rio Middle School


### New Playground Location





# Maintenance Department – Monthly Service Requests

Support Tickets 2-1-2018 thru 3-1-2018

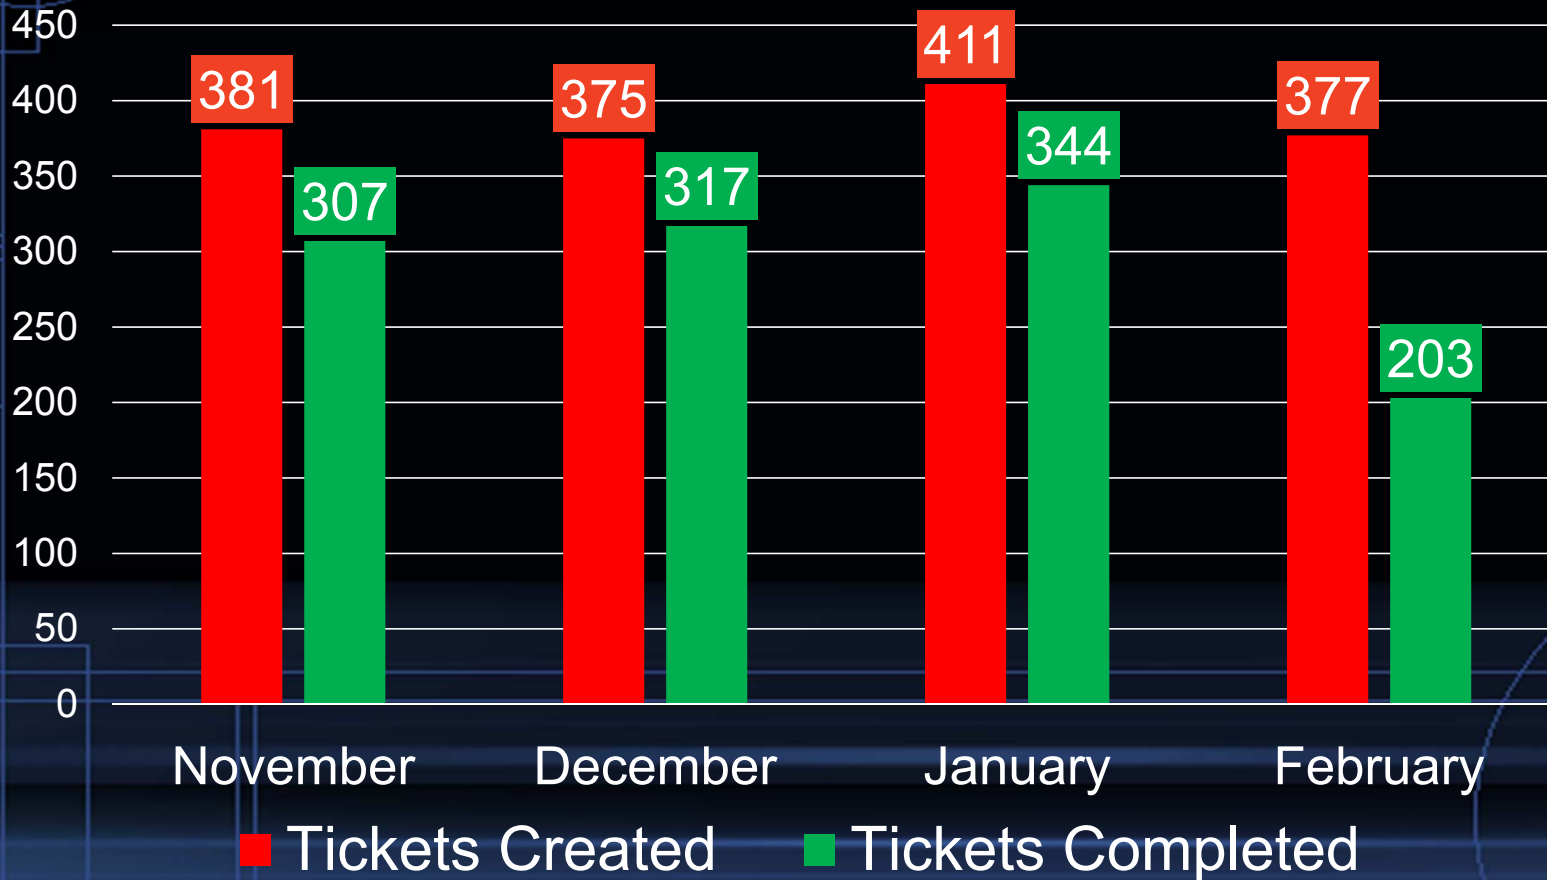

Within 30 Days = 174  
60 Days = 3  
90 + Days = 8

The background is a dark blue gradient with a complex geometric pattern of thin, light blue lines and circles. The lines form a grid-like structure with various rectangular and circular shapes, some overlapping. The circles are of different sizes and are scattered across the frame, some partially cut off by the edges. The overall effect is a technical or architectural aesthetic.

Questions?
