

Facilities & Construction Report

PROJECT STATUS 2/19/2018

Operations @ A Glance

- New Construction
 - Laughlin Elementary STEM Magnet School
 - Stadium Bleacher Project
 - Portable Buildings
- Technology Department
 - Monthly Service Requests
- Maintenance Department
 - Campus Improvements
 - Monthly Service Requests

New Construction

Laughlin Elementary STEM Magnet School

- ✓ Arrival of first modular - 2-16-18
- Set crew arrives to join buildings - 2-23-18
- Set crew finishes - 3-15-18
- Walkways and parking lot finish - 4-1-18
- Interior work, data intercom - 5-1-18
- Security finished - 5-1-18
- Complete all work - 5-15-18



New Construction

Walter Levermann Ram Stadium – Bleachers



- ▣ Board Approved – 1/22/2018
- ▣ Demo of Bleachers - Scheduled – 2/12/2018 – Delayed (Rescheduled to 2/19/2018)
- ▣ Schematic Drawings of Storage, Restrooms, and Concession Stand – March 2018
- ▣ Installation of New Bleachers – 5/1/2018


Surplus Portable Buildings - Local Policy

- CI (Local) The Superintendent or designee is authorized to declare District materials, equipment, and supplies to be unnecessary and shall dispose of unnecessary materials, equipment, and supplies for fair market value.



Technology Department – Monthly Service Requests

Support Tickets 1-1-2018 thru 2-1-2018

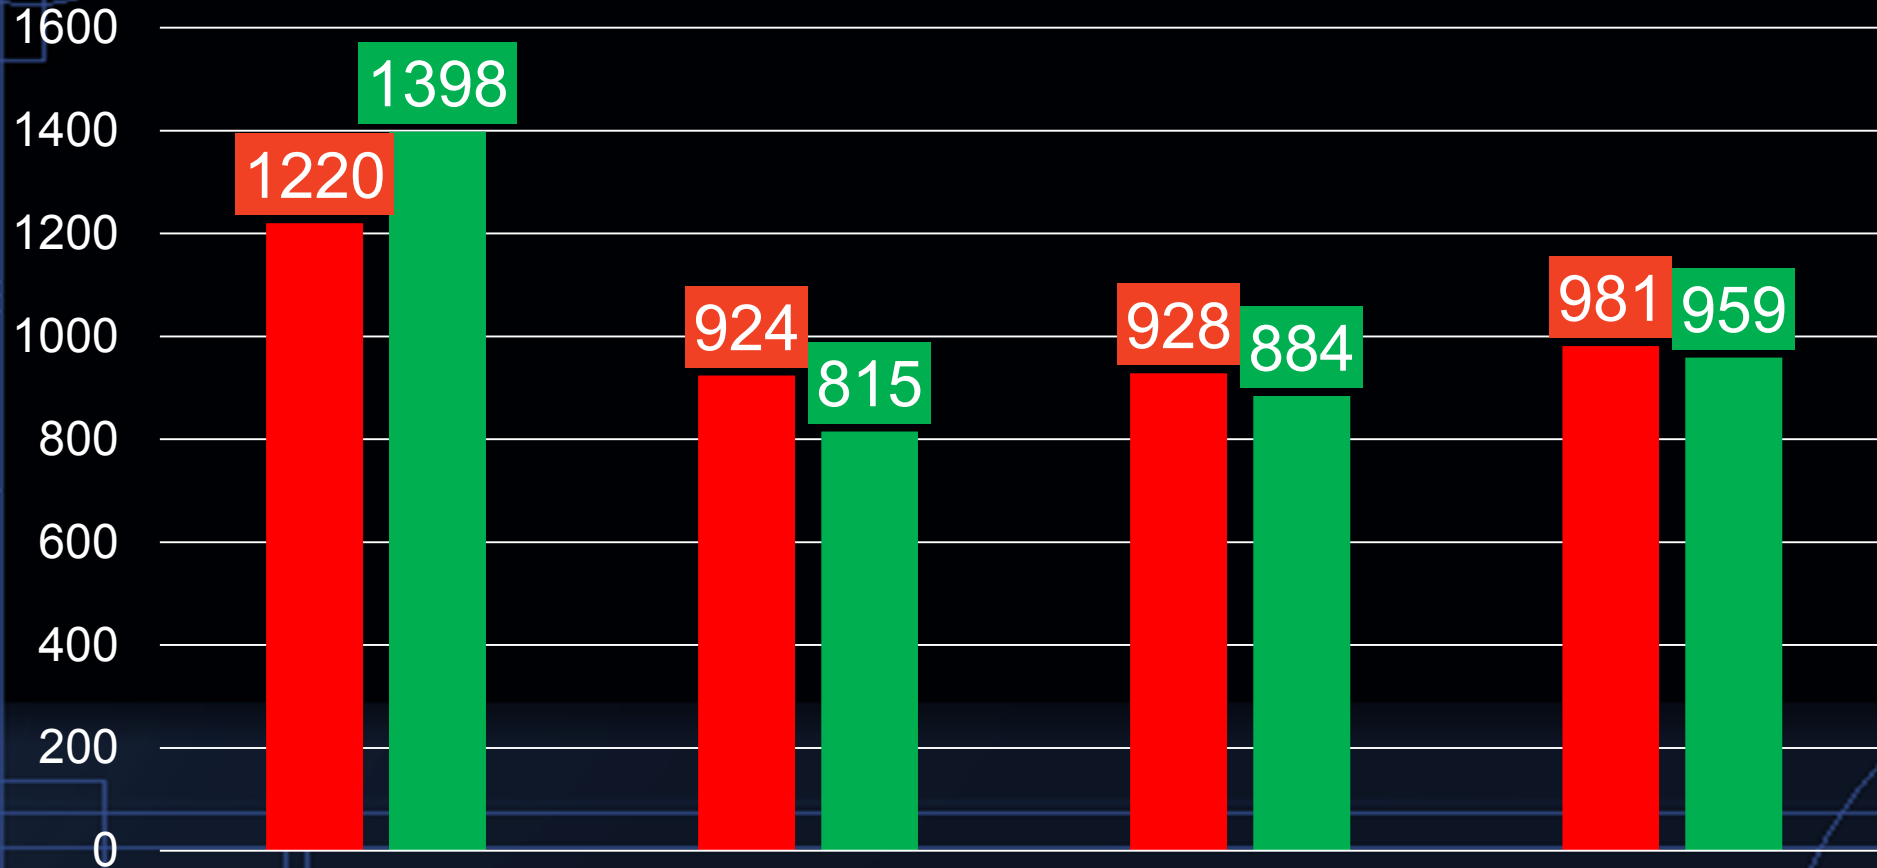

Within 30 Days = 22
60 Days = 0
90 + Days = 0

October November December January

■ Tickets Created ■ Tickets Completed

Maintenance Department

Campus Improvements - Athletics Department

Freshman Baseball Field

Softball Batting Cage



Maintenance Department

Campus Improvements – Del Rio Middle School


New Playground Location



- Project “Kick Off” - 3-1-18
- Installation of Playground Equipment - 3-12-18
- Installation of Fence & Gates - 3-19-18
- Installation of Fall Material - 3-21-18
- Painting - 3-27-18
- Complete all work - 3-27-18

Maintenance Department – Monthly Service Requests

Support Tickets 1-1-2018 thru 2-1-2018

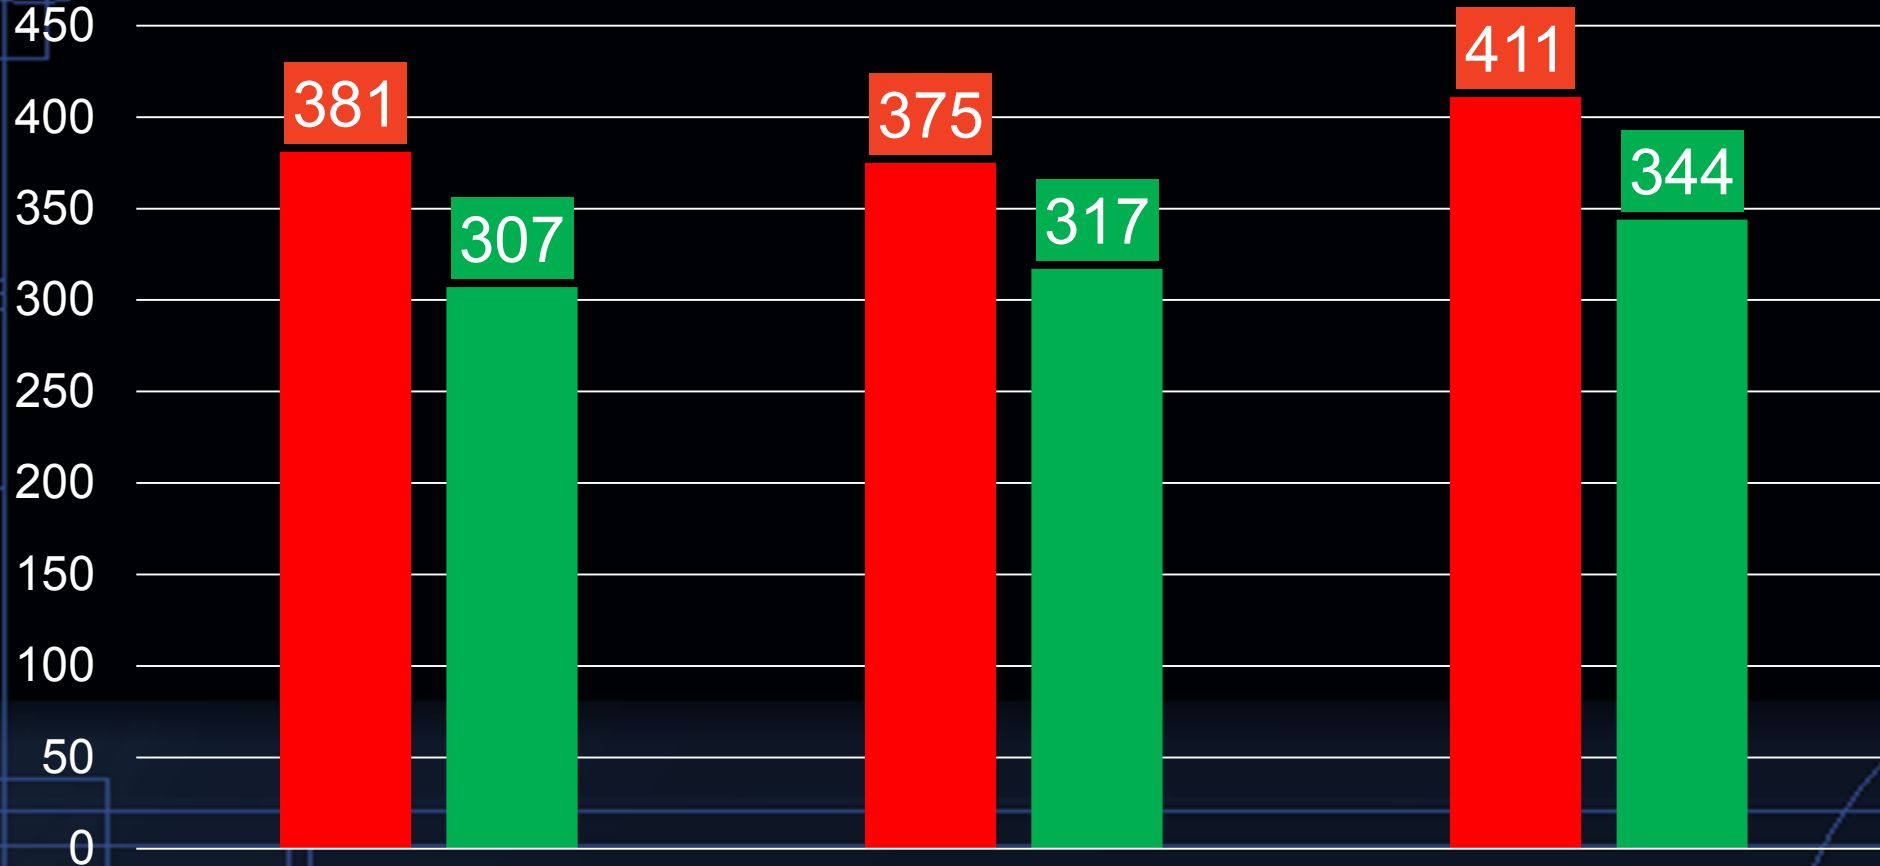

Within 30 Days = 67
60 Days = 30
90 + Days = 30

November

December

January

■ Tickets Created

■ Tickets Completed

The background is a dark blue gradient with a complex pattern of thin white lines. These lines form a grid-like structure with various geometric shapes, including circles, squares, and rectangles, some of which are partially cut off by the edges of the frame. The overall effect is a technical or architectural drawing style.

Questions?
