

SAN FELIPE DEL RIO CISD FACILITIES & CONSTRUCTION REPORT



Project Status: June 21, 2021

Presented By: Les Hayenga / Chief Operations Officer



Del Rio High School Stadium Track Replacement






- ✓ G.C. Board Approved 4/19/21
- √ Work Begins 6/21/21
- Complete Track Removal 6/25/21
- Complete Base Installation 7/7/21
- Complete Spray-on Track 7/15/21

Del Rio Freshman School





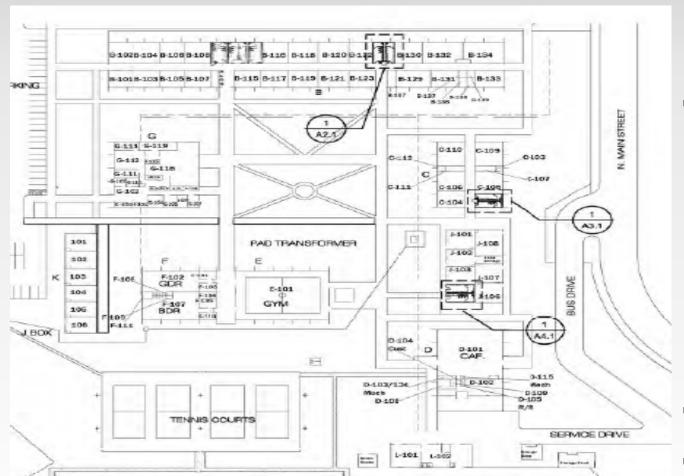


- Pre Construction
 - Campus Leadership to Review Plan 6/23/2021
 - Board Approval of G.C. 6/24/2021
 - Contract Approval 6/24/2021
 - Required Documents Submittal 7/2/2021
 - Building Permit Obtained 7/23/2021
- Work Begins 7/26/2021
- Worked Completion 1/28/2022

Del Rio Freshman Campus

Life Skills Renovation



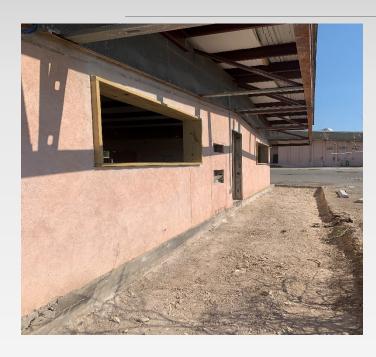



- Phase One Exterior
 - ✓ G.C. Board Approved 11/16/2020
 - √ Work Begins 3/23/21
 - ✓ Demolition Completed 4/23/21
 - Complete Windows & Doors Installation 7/23/21
 - Complete New Clad Installation 8/20/21
 - Complete Clearstory Installation 9/03/21
 - Complete Phase 1 Work 9/24/21

Buena Vista Elementary Entryway & Main Office Renovation

Start Date: 6/14/2021




Conference Room Teacher's Lounge Counselor Counselor Reception Nurse Principal

- ✓ Pending Board Approval 05/17/21 Asbestos Abetment
- ✓ Asbestos Abatement 06/14/21
- New Construction 06/28/21
 - Two Counselor Offices
 - Conference Room
 - Front Reception Area
 - Principals Office
 - Staff Lounge
- Upgrade Electrical & Network: 06/28/21
- Interior Painting: 7/12/21
- Flooring: 07/19/21
- Work Completed 8/6/2021

New Elementary Campus Project Status



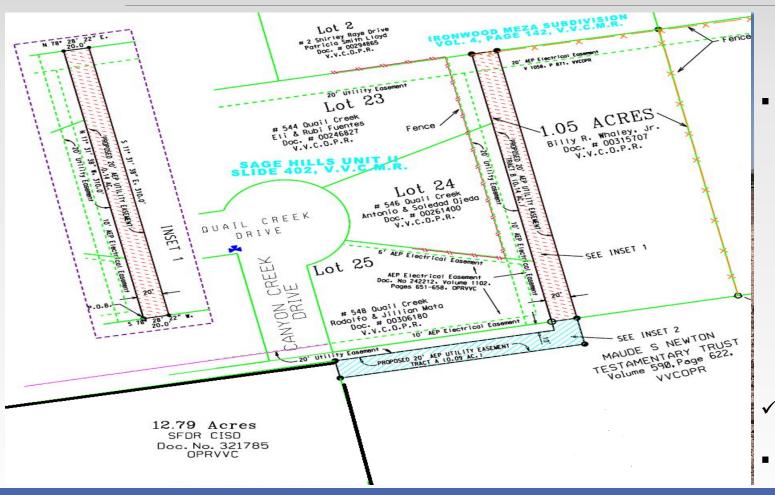

- Pre Construction
 - ✓ General Contractor Selected 4/6/2021
 - ✓ Contract Approved 4/19/2021
 - ✓ Required Documents Submitted 5/15/2021
 - ✓ Building Permit Obtained 6/4/2021
 - ✓ Ground Breaking 6/5/2021
- ✓ Work Begins 6/7/2021
- Worked Completed 5/27/2023

Special Education Department Renovation & Relocation

Start Date: 2/8/2021




- ✓ Partition Builds 2/15/2021
- ✓ Exterior Painting: 2/25/2021
- ✓ Upgrade Electrical & Network: 5/19/2021
- ✓ Asphalt Replacement: 5/27/2021
- Drywall Tape & Float: 6/23/2021
- Interior Painting: 6/30/2021
- New Flooring: 7/13/2021
- Fire/Alarm System: 7/16/2021
- Relocate Special Ed Staff 8/2/2021

Transportation Department


Fuel Distribution System



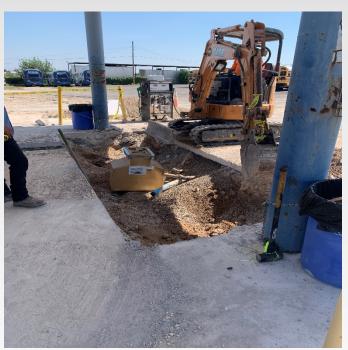



- ✓ General Contractor Selected 12/14/2020
- √ Work Begins 3/23/2021
- ✓ Fuel Tank Installation 4/30/2021
- Work Completed 7/12/2021

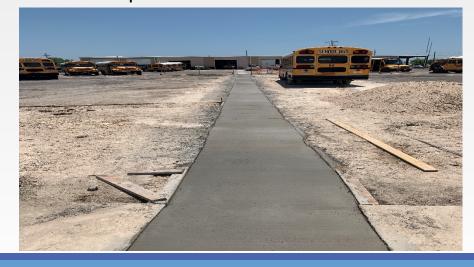

TPO Roofing Repairs

Original Contract Amount \$750,820.00

- North Heights Elementary Classrooms 101-124 Elementary A-B
- Student Performance Center
- Irene C. Cardwell Elementary Library
- Dr. Fermín Calderon Elementary
 Main Building
 Gymnasium
 Special Education
- San Felipe Memorial Middle School Building B North Building B South

AAA Roofing, LLC

Revised Contract Amount \$930,820.00

- North Heights Elementary
 Classrooms 101-124
 Elementary A-B
- Student Performance Center
- Irene C. Cardwell Elementary Library
- Dr. Fermin Calderon Elementary
 Main Building
 Gymnasium
 Special Education
- San Felipe Memorial Middle School Building B North Building B South
- Del Rio Middle School

 A Portion of the 8th Grade Roof

Non-TPO Roofing Repairs

Original Contract Amount \$1,330,400.00

- CTE
- Early College
- Buena Vista Elementary Library
- Irene C. Cardwell Elementary Building E Cafeteria
- San Felipe Memorial Middle School Gymnasium Building D Building E Library

Advantage USAA, Inc.

Revised Contract Amount \$1,062,190.00

Del Rio High School ROTC Building

Library

- Lamar Elementary
 Main Building (East and West Ends)
- Irene C. Cardwell Elementary Building E Cafeteria
- San Felipe Memorial Middle School Kitchen Building D Building E



QUESTIONS?

