



SAN FELIPE DEL RIO CISD FACILITIES & CONSTRUCTION REPORT

School Board Meeting – June 16, 2025



SAN FELIPE DEL RIO CISD FACILITIES & CONSTRUCTION REPORT

Construction Projects:

- Cody Wardlaw Gymnasium Renovation
- HVAC Equipment Replacement – DRMS, Lamar & Del Rio Freshman
- SFMMS /Cody Wardlaw Gym Fence



SAN FELIPE DEL RIO CISD FACILITIES & CONSTRUCTION REPORT

Cody Wardlaw Gymnasium Renovation:

	Contractor	Begin Date	End Date	
Roofing	AAA Roofing	12/19/24	01/31/25	✓
Plumbing	Texas Chillers System	12/01/24	05/23/25	✓
HVAC	Amistad Heating and A/C	01/06/25	06/30/25	
Electrical	Dynamic Pro Electric	12/01/24	07/31/25	
Windows & Doors	Central Glass & Mirror	01/17/25	06/30/25	
Gym Floor (Ph. 1)	QHF Sports	01/06/25	01/15/25	✓
Gym Floor (Ph. 2)	QHF Sports	05/01/25	05/31/25	
Painting	Legacy Properties	03/24/25	06/30/25	
Flooring/Wall Tile	Legacy Properties	03/31/25	04/30/25	✓



SAN FELIPE DEL RIO CISD FACILITIES & CONSTRUCTION REPORT


Cody Wardlaw Gymnasium Renovation:





SAN FELIPE DEL RIO CISD FACILITIES & CONSTRUCTION REPORT

Cody Wardlaw Gymnasium Renovation:

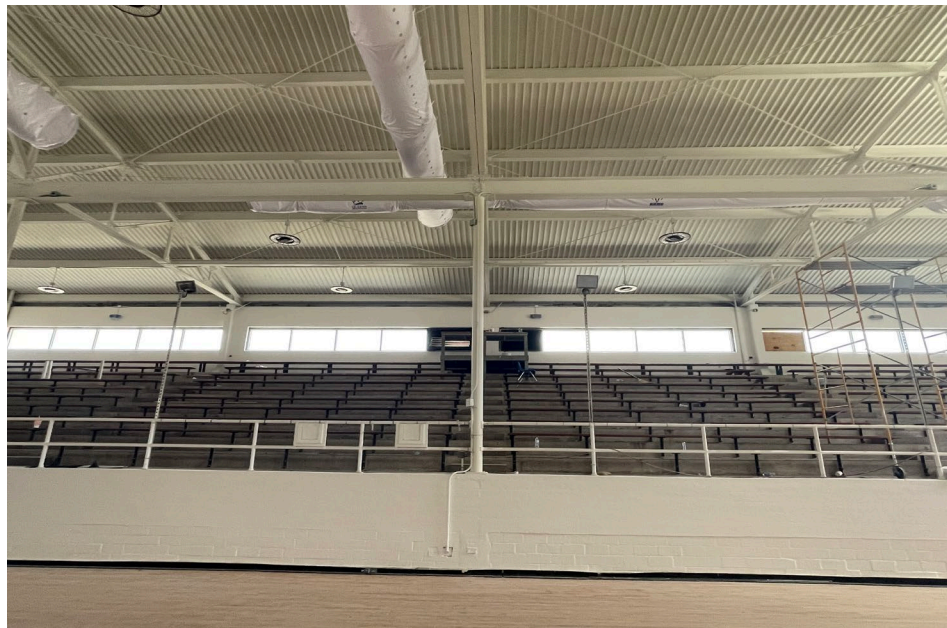

Maintenance Dept. Ticket Summary



March 1, 2025– May 31, 2025

Maintenance Work Order Status

Work Orders	90 Days Created Ticket Total	0-15 days	16-30 days	31-60 days	61-90 days
Created	983	138	166	334	345
Open	92	23	13	35	21
Closed	891	115	153	299	324
% Completed	91%	83%	92%	90%	94%

Technology Dept. Ticket Summary



March 1, 2025– May 31, 2025

Technology Work Order Status					
Work Orders	90 Days Created Ticket Total	0-15 days	16-30 days	31-60 days	61-90 days
Created	3215	390	541	938	1346
Open	274	75	28	42	129
Closed	2941	315	513	896	1217
% Completed	91%	81%	95%	96%	90%

Transportation Dept. Ticket Summary



March 1, 2025– May 31, 2025

Transportation Work Order Status					
Work Orders	90 Days Created Ticket Total	0-15 days	16-30 days	31-60 days	61-90 days
Created	260	28	47	60	125
Open	11	3	5	3	0
Closed	249	25	42	57	125
% Completed	96%	89%	89%	95%	100%



SAN FELIPE DEL RIO CISD
FACILITIES & CONSTRUCTION
REPORT

Questions?
